

Construction activity continues for the Prince of Wales Hospital Integrated Acute Services Building (IASB); the first stage of the Randwick Campus Redevelopment and the catalyst project for expanding the world-class health, research and education facilities at the Randwick Health & Innovation Precinct.

We thank you for your patience while we expand our world-class health, research and education facilities.

**Key activities continuing throughout June include:**

***Integrated Acute Services Building construction;***

Roof steelwork, façade installation and internal fit-out including walls, floors and services.

***Hospital Road construction;***

Piling in Delivery Drive for the new clinical link bridge to connect the IASB with the existing hospitals campus, demolition of temporary structures, bulk excavation and service upgrades with appropriate closures and diversions in place.

***Hospital campus car park activities;***

Connection of the recently installed bulk oxygen storage tank to existing infrastructure and preparation works for future piling for the public link bridge.

***Out of hours equipment deliveries.***



*Façade installation progressing on the IASB*

**Upcoming activities include:**

**Temporary weekend closures of Delivery Drive and Hospital campus loading docks;**

Out of hours construction activity including piling works for the link bridges connecting the IASB to the existing hospitals campus.

To enable this activity a piling rig will be delivered prior to the weekend closure and outside of peak traffic times to the Hospital Road site, via Barker Street and removed after each weekend closure. Delivery and removal of the rig will take approximately one hour to complete. It is a requirement of Transport for NSW that deliveries of this size occur out of hours. A specific notification will be issued to local stakeholders once the dates and times are confirmed.

**Closures are planned as follows:**

<b>Friday 18 June to Sunday 20 June</b>	Planned closure*
<b>Friday 25 June to Sunday 27 June</b>	Planned closure*
<b>Friday 2 July to Sunday 4 July</b>	Contingency closure*

**\*All closures will occur from 5:00pm Friday to 10:00pm Sunday**

**Work to upgrade the Ausgrid High Voltage underground network;**

Works will involve low impact cable pulling and installation along Hospital Road and Botany Street. For traffic and safety reasons this work will occur out of hours, between **6:00pm and 6:00am from Sunday 20 June to Saturday 26 June**, and is approved under an Ausgrid authority. Power supply to private properties will be maintained during this work.

**Southern tower crane is planned for removal from site during June;**

To enable this work to occur, an oversized mobile crane will be delivered to the site out of hours, via Hospital Road south. It is a requirement of Transport for NSW that deliveries of this size occur out of hours.

We encourage you to get in touch if you have any questions or feedback, or would like to receive email updates:

Community Contact 1800 571 866 (24hrs)

[randwickcampusredevelopment@health.nsw.gov.au](mailto:randwickcampusredevelopment@health.nsw.gov.au)

[www.randwickcampusredevelopment.health.nsw.gov.au](http://www.randwickcampusredevelopment.health.nsw.gov.au)

### Minimising construction impacts

We are committed to minimising the impact of our works where we can. All construction activities are carried out with the health and safety of the local community as our top priority. We endeavour to keep noise, dust and vibration to a minimum. Some ways we do this include:


- truck minimisation periods during peak times to maintain traffic flow into the car parks from Hospital Road with construction vehicles prohibited to use Magill Street to access Hospital Road
- traffic control and safety exclusion zones established to ensure worker, pedestrian and vehicle safety
- environmental measures in place to manage light spill, dust, noise and vibration
- noise, dust and vibration monitoring devices in use 24 hours per day, 7 days per week
- delivery and removal of large plant and equipment to occur out of hours as per requirement of Transport for NSW
- high impact works to be conducted during standard hours with respite periods during rock-breaking activities
- coordinating works to ensure hospital operations continuity.

### Current construction hours

Current approved construction hours are **Monday to Friday 6:00am – 10:00pm and Saturday 7:00am – 5:00pm**. There will be no work on Sunday unless prior approval is granted.

Other work may be planned outside of the approved construction hours to ensure the safety of workers, pedestrians and motorists, and to minimise impacts to local traffic and hospital access. Any out of hours work will continue to be communicated in advance.

### Map of Construction Activity June 2021

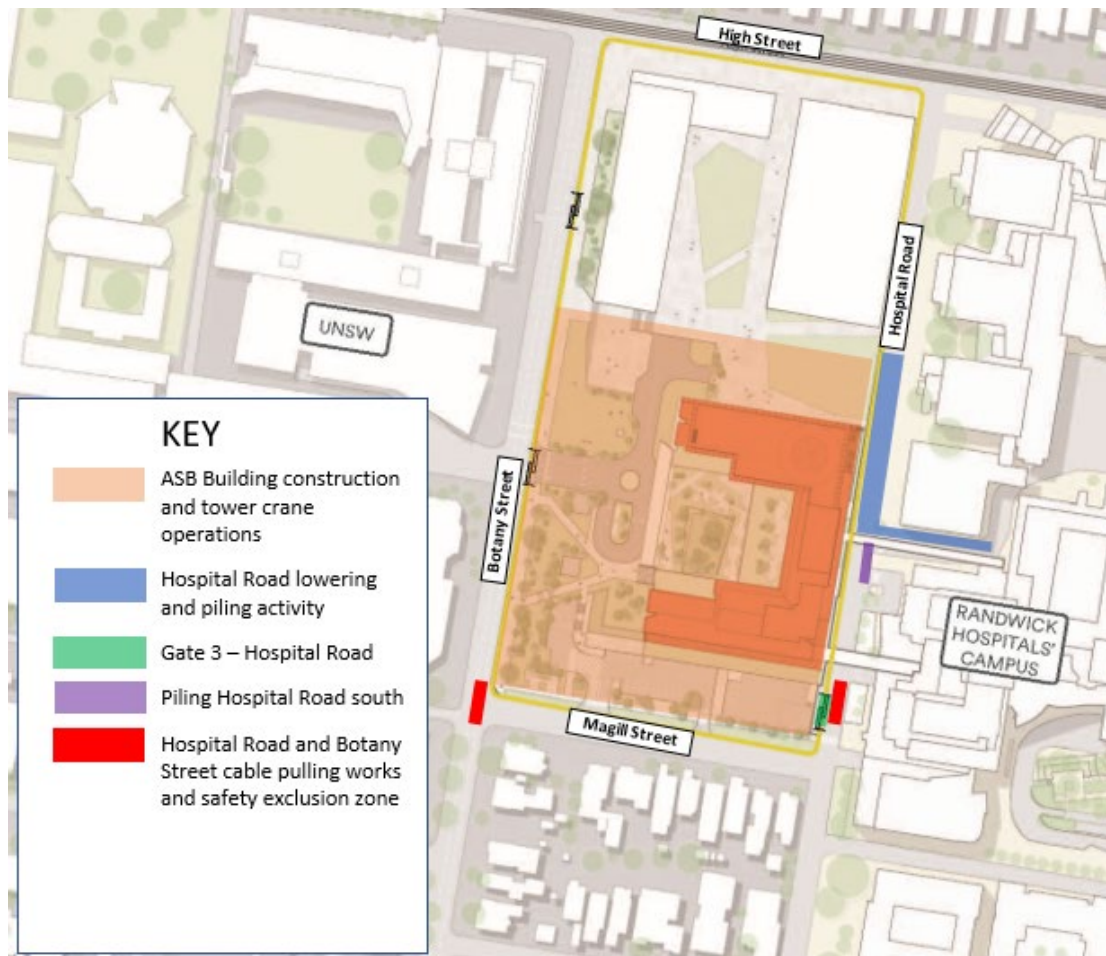

We encourage you to get in touch if you have any questions or feedback, or would like to receive email updates:

Community Contact 1800 571 866 (24hrs)

[randwickcampusredevelopment@health.nsw.gov.au](mailto:randwickcampusredevelopment@health.nsw.gov.au)

[www.randwickcampusredevelopment.health.nsw.gov.au](http://www.randwickcampusredevelopment.health.nsw.gov.au)
