

Construction Update

Construction activity continues within the Randwick Campus Redevelopment site, which incorporates the Prince of Wales Hospital Acute Services Building (ASB) and associated UNSW Eastern Extension, along with the future Sydney Children's Hospital Stage 1 and Minderoo Children's Comprehensive Cancer Centre (SCH1/MCCCC) building, and UNSW's Health Translation Hub (HTH).

Visit the Randwick Campus Redevelopment website at randwickcampusredevelopment.health.nsw.gov.au to learn more about each of these exciting projects and read our latest news stories.

Upcoming activities

Sydney Children's Hospital Stage 1 and Minderoo Children's Comprehensive Cancer Centre

Structural works, including formwork, steel fixing and concrete pouring to establish each level of the new building continues to progress. By late October, the structure will reach level three, which will house the new medical short stay inpatient unit, along with part of the new Minderoo Children's Comprehensive Cancer Centre.

To support ongoing construction and in preparation for internal fit-out activities, early stages of formwork removal in the lower levels of the new building, such as the future loading dock, is underway.

Night works will be carried out during October (weather permitting) to finalise the installation of a protective overhead gantry hoarding at the corner of

High Street and Hospital Road, which may result in intermittent construction noise. Additional out of hours activities to survey existing Sydney Water Authority assets is also planned for October. Detailed information will be provided to nearby stakeholders ahead of activities commencing.

Prince of Wales Hospital Acute Services Building and UNSW Eastern Extension

Internal fit-out activities for the additional inpatient units within the new ASB are nearing completion, in readiness for commissioning activities to commence.

Internal fit-out activities within the UNSW Eastern Extension also continue to progress. Works include partitioning and service installation on the lower levels of the 10-storey structure.


UNSW Health Translation Hub

Construction activities are well underway on the site of the future UNSW Health Translation Hub. Structural piling works have now been completed, with remediation and excavation works continuing.

Ongoing site establishment activities are planned during October, including site shed and storage compound setup.

Works to temporarily remove three light poles on a section of Botany Street adjacent to the construction site will see a temporary footpath closure for a period of approximately one week. Pedestrian diversions to the western footpath will be in place for the duration of works.

Map of construction activities October 2023

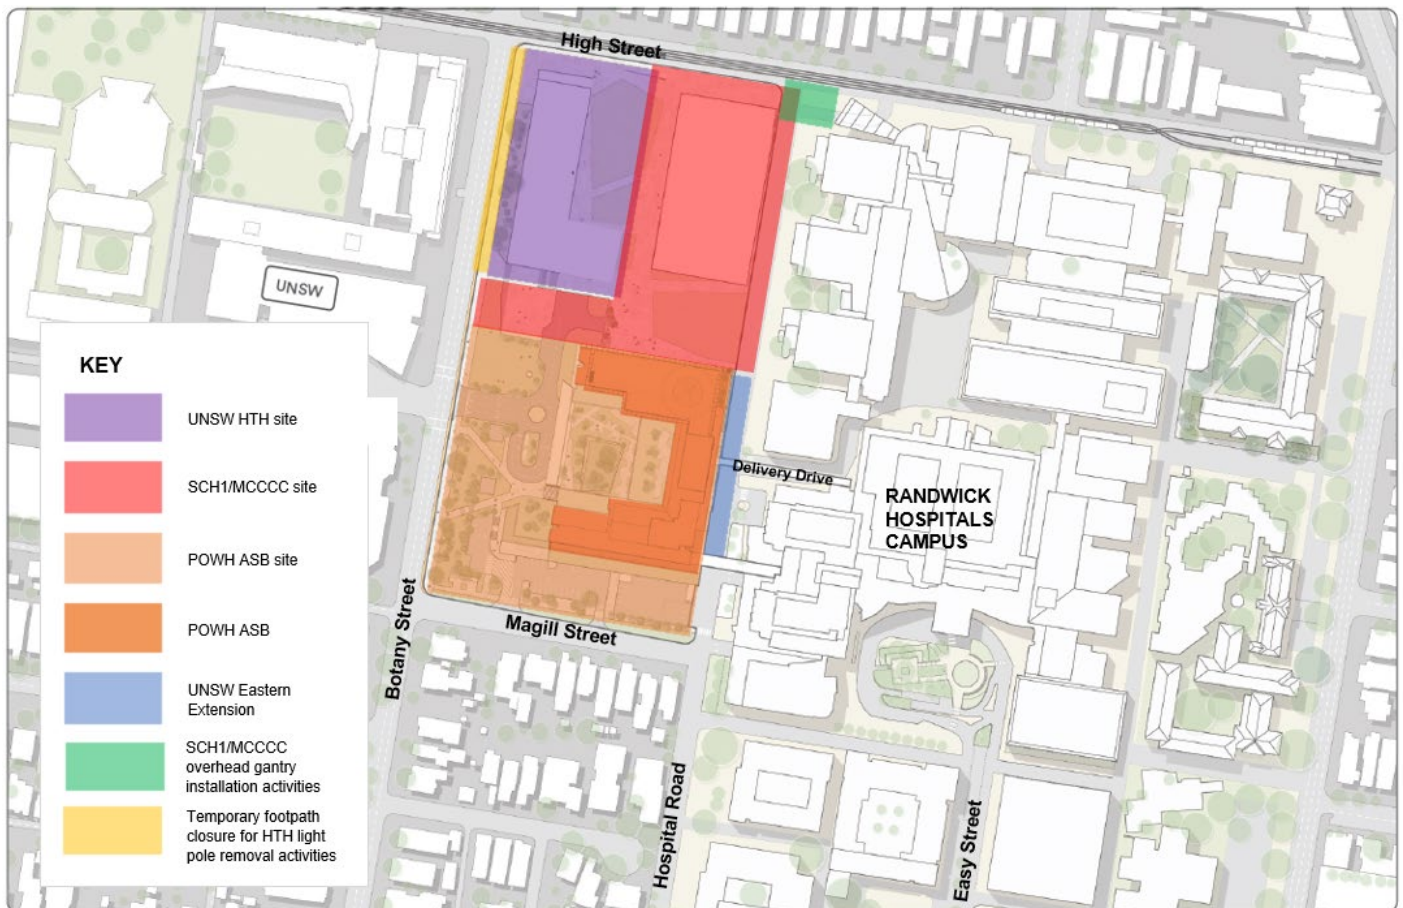

Managing construction activities

We are committed to minimising the impact of our works. All construction activities are carried out with the health and safety of the local community and site workers as our top priority.

We endeavour to keep noise, dust and vibration to a minimum.

Where possible, activities are scheduled during approved site hours of **Monday to Friday, 7am to 6pm and Saturday, 8am to 5pm**. Work may be delayed or rescheduled due to weather or unforeseen circumstances such as workforce availability.

Out of hours work will continue to be communicated directly to affected stakeholders. All activity dates and times are subject to change.

Please note that service upgrades unrelated to the redevelopment project may also be undertaken by other agencies at any given time without notification.



View our [interactive map](#) for the latest information on construction activities across campus, or to learn more about each of the Randwick Campus Redevelopment projects.
