

Construction Update

The NSW Government is investing over \$1 billion in the Randwick Health & Innovation Precinct, strengthening health, research, education and innovation outcomes to ensure NSW is at the forefront of health research and education internationally.

Main Works for the new Prince of Wales Hospital Acute Services Building are nearing completion, and the Works for the Sydney Children's Hospital Stage 1 and Minderoo Children's Comprehensive Cancer Centre Redevelopment are underway.

Activities in August 2022

Acute Services Building construction

Across all floors of the Acute Services Building, installation of final finishes continues as hospital users participate in witness and validation testing of building services and systems.

Landscaping at the Botany St Main Entry forecourt and the Emergency Department entry adjacent to Magill Street will continue in August.

Works for the clinical link bridge, public link bridge and the UNSW Eastern Extension structure are ongoing and will continue throughout August. Additional information about localised activities will be provided to affected stakeholders.

Construction works for the staff End of Trip Facility on level B3 of the campus carpark will continue in August.

Sydney Children's Hospital Stage 1 and Minderoo Children's Comprehensive Cancer Centre construction

Early and Enabling Works for the Sydney Children's Hospital Stage 1 and Minderoo Children's Comprehensive Cancer Centre continue on the northern portion of the site and Hospital Road north. Activities include site remediation, service investigations and installation of new electrical infrastructure under Hospital Road and the High Street footpath.

There will be changes to hoarding alignments on Hospital Road north throughout August. Pedestrian access on the existing footpaths will be maintained.



Works progressing for the public link bridge connecting the new Acute Services Building to the hospital campus.

Hospital Road south activities

Work on Hospital Road south to repair and improve the road and footpaths near the B3 carpark entry/exit is planned for August.

Pedestrian access will be managed through appropriate diversions. Signage and/or traffic control will be in place to assist pedestrians, where required. Further information will be provided to affected stakeholders ahead of the works.

Botany Street activities

Construction planning for the new four-way signalised intersection on Botany Street continues.

The intersection will be installed on Botany Street, between High Street and Magill Street, to provide safe pedestrian and vehicle access to the Prince of Wales Hospital Acute Services Building, the Sydney Children's Hospital Stage 1 and Minderoo Children's Comprehensive Cancer Centre, UNSW Health Translation Hub and UNSW Kensington Campus.

Further information will be provided to affected stakeholders ahead of the works commencing.

Francis Martin Drive activities

Works to widen the footpath on the southern side of Francis Martin Drive will commence in August. There will be minimal impacts to vehicles, bikes, and pedestrian access. Signage and traffic control will be in place to assist, where required, with priority given to ambulances.

Magill Street upgrade

Landscaping activities on Magill Street are scheduled for the upcoming weeks. This work will occur in localised work zones. Magill Street remains accessible to residents throughout the works.

Upcoming out of hours work

Hospital Road and Delivery Drive activities

Temporary weekend closures of the hospital loading docks are planned to continue throughout August. Closures will occur from 5pm Friday through to 10pm Sunday supporting a range of construction activities on Hospital Road and Delivery Drive.

Critical works may occur past 10pm in the case of inclement weather or delays to ensure the loading docks can reopen safely to maintain hospital operational continuity.

Resurfacing of Delivery Drive and Hospital Road towards the Black Dog Institute is expected to take place in August. These works are planned to occur over two consecutive nights, followed by an additional night, a week later for road line-marking (weather permitting)

Night works for planned electrical power outages and system cutovers at Hospital Road north is upcoming in

August. Detailed information of related impacts will be provided to affected stakeholders ahead of works commencing.

Managing construction activities

We are committed to minimising the impact of our works where we can.


All construction activities are carried out with the health and safety of the local community as our top priority. We endeavour to keep noise, dust and vibration to a minimum.

Where possible, activities are scheduled during approved site hours **Monday to Friday, 7am to 6pm and Saturday, 8am to 5pm.**

Work may be rescheduled due to weather or unforeseen circumstances such as workforce availability. Any out of hours work will continue to be communicated in advance directly to affected stakeholders.

Thank you for your patience while we progress this important work.

Map of construction activities August 2022

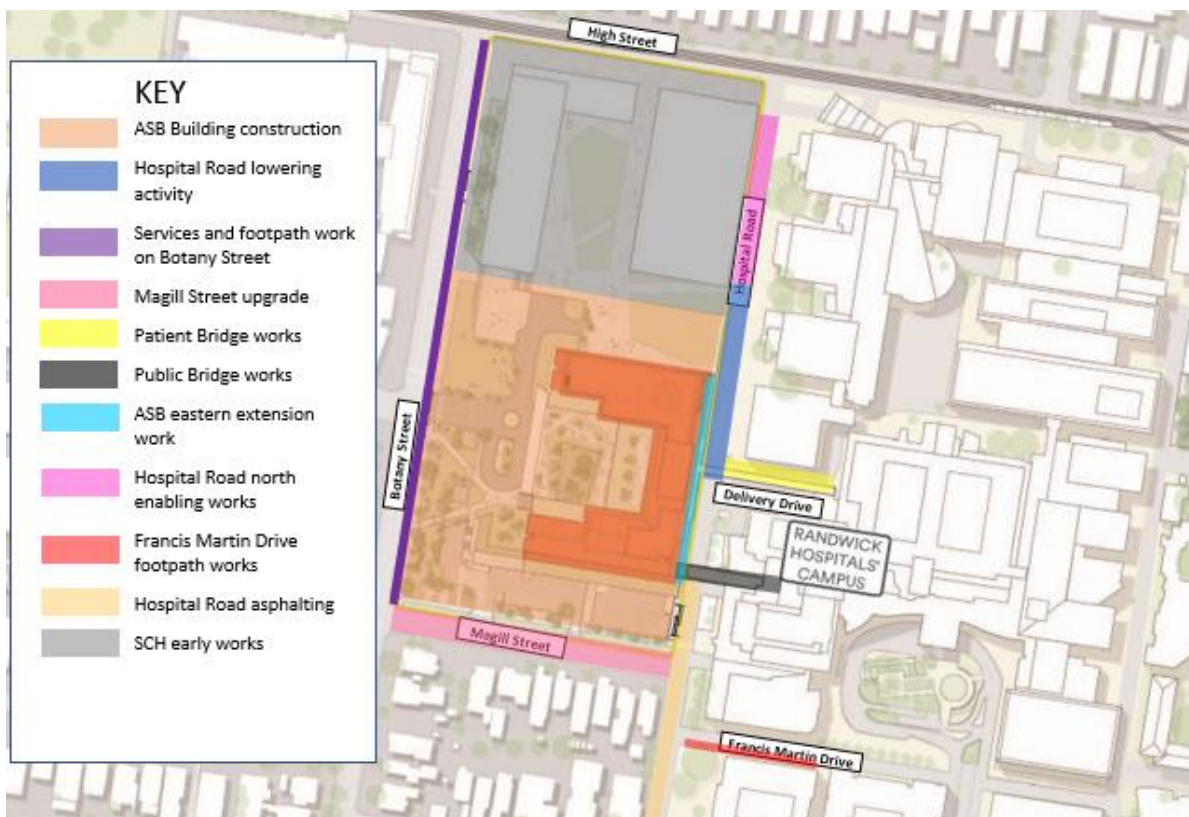

1800 571 866



randwickcampusdevelopment@health.nsw.gov.au



randwickcampusredevelopment.nsw.gov.au
